



SAN GABRIEL

Public Works

STREETS | PARKS | ENGINEERING
UTILITIES | FACILITIES | FLEET

Public Works Project Delivery Report

August
2017

San Gabriel Public Works delivers reliable infrastructure & welcoming public spaces by designing, constructing, operating & maintaining the City's streets, parks, utilities, facilities & fleet.

PROJECTS IN CONSTRUCTION

Great Streets Ahead

- **ACE Haul Route Restoration**

The restoration of pavement and associated work on more than 3.5 miles of City street is nearly complete. **Agostino Road, Del Mar Ave, Grand Avenue, Main Street, Santa Fe Ave, and Mission Road** are substantially complete with utility adjustments and some striping remaining. **San Gabriel Blvd** between Valley Blvd and Mission Road is also complete, while work continues south of Valley Blvd, followed by north of Mission Road.



- **Del Mar Avenue Pavement Rehabilitation Project Phase 3 (Saxon Avenue to Norwood Place)**

Council awarded the construction contract in April and work began in June. The project involves reconstructing the existing pavement, installing new curb ramps, and restriping of the roadway to include bike lanes. The final paving was completed on August 1. Striping will be completed by mid-August.



- **San Gabriel Blvd/Mission Road Intersection Improvements**

Sequel Contractors, Inc. has been working on street and sidewalk improvements, construction of a right turn lane from Mission Road to San Gabriel Blvd., new traffic signals, and drainage facilities. Utility companies are currently working to relocate their facilities to accommodate the new improvements, and some of the paving has been completed on the south and west legs of the intersection. The contractor began work in April, and the project is scheduled to be completed in October 2017.




Marshall Community Park

Construction of this great new park is moving swiftly with grading, utilities, lighting, walkways and playground equipment complete. Current work includes the basketball court, restroom building, and fence installation. A Grand Opening ceremony will be held this fall – details will be announced soon. *The photo below shows the site as of August 1.*



Vincent Lugo Park Fitness Equipment & Picnic Shelters

Construction of the three new picnic shelters and installation of adult fitness equipment around the park is currently underway and will be completed in September.

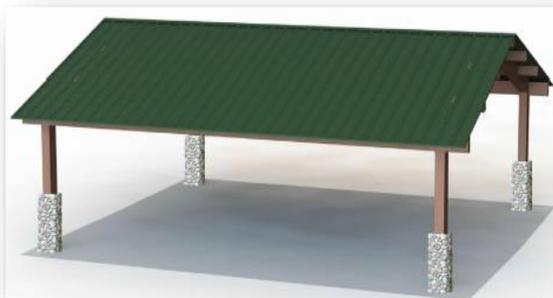

City Hall Renovations

This project will improve customer service, efficiency and safety for several Departments in City Hall, including the City Clerk, Finance, and Human Resources Departments. Security features have been added to Finance, a desk for the new City Clerk Greeter position is currently being constructed and the upstairs offices will be remodeled starting in late August. The project is expected to be completed by this fall. In addition to the interior renovations, the exterior of City Hall will be repainted in September.



PROJECTS IN DESIGN/PRE-CONSTRUCTION

2017-18 Great Streets Pavement Project

City Council awarded the Professional Service Agreement for Design 2017-2018 Great Street Project to Civil Works Engineers on June 20. The Project consists of two phases of pavement rehabilitation on various public streets located in the City. The project kickoff meeting was held on July 13. We anticipate completing the design for Phase 1 in December 2017 and Phase 2 in April 2018. The streets that are included in the design include:

Phase 1

- San Marino Avenue (from Longden to Las Tunas)
- Warner Lane (from San Marino to west end)
- Oak Lane (from San Marino to west end)
- Broadway (from Mission Drive to Junipero Serra)
- Alanmay (from Broadway to Live Oak)
- Cresta Avenue (from Las Tunas to Hermosa)
- Earle Street (from Las Tunas to Elm)

Phase 2

- Bilton Way (from Fairview to Orange)
- Orange Street (from Del Mar to Montecito)
- Santa Anita Street (from Mission Road to Mission Drive)
- Arroyo Drive (from Santa Anita to Mays Alley)
- Carmelita Drive (from San Marcos to Mission Drive)
- San Marcos Street (from Santa Anita Street to Mays Alley)
- Alley west of City Hall (from Santa Anita Street to McGroarty)

Del Mar Avenue Phase 2 (Bencamp Street to Chestnut Avenue)

Design is underway for this project which involves the repaving of this segment of Del Mar Avenue and replacement/upgrade of the sanitary sewers below Del Mar Avenue. The design will be completed by the end of the year and construction will start in early 2018.

Del Mar Avenue - Alhambra Wash Bridge Replacement

This City project is funded primarily by the Federal bridge replacement program and is being designed by LA County Public Works. The project was advertised for bids in June, and bids were opened this month. The County is analyzing the bids to determine the lowest responsive bidder, and we anticipate that a construction contract will be approved by the Board of Supervisors in October. Construction will begin in early 2018, would run through two dry seasons due to restrictions on the Alhambra Wash, and will be completed in 2020.

Broadway/Walnut Grove Intersection Improvements

Design of this federally-funded project is complete. Right-of-way appraisals and negotiations have taken longer than anticipated. A portion of the utility relocations for the project has been completed. Construction is anticipated to begin in 2018 and will be coordinated with the school calendar to minimize impacts.

FOR MORE INFORMATION...

If you would like more information on any of these projects, please contact the Public Works Department at (626) 308-2825.

City of San Gabriel
Public Works Department
917 East Grand Avenue
San Gabriel, California 91776
(626) 308-2825
